

General news





Activités 2024-2025 (liste non exhaustive)

- Christian Olivetto : nouveau RT ET France
- Diverses réunions
 - 02/2024 : visite vide et cryo à Kagra
 - 03/2024 : workshop R&D France @Marseille ([indico](#))
 - 05/2024 : XIV ET Symposium @ Maastricht ([indico](#))
 - 09/2024 : workshop on ET-LF TM Tower integration concepts @ Elba ([indico](#))
 - 10/2024 : ET France @ Caen ([indico](#))
 - 11/2024 : III ET annual meeting @ Varsovie ([indico](#))
 - 11/2024 : CODEC ([indico](#)) => validation des implications RH et budget mission
 - 02/2025 : visite du ministre de la recherche Néerlandais
 - 03/2025 : rencontre avec les responsables Virgo et ET France ([indico](#))
 - 03/2025 : II workshop on ET-LF TM Tower integration concepts @ IJCLab ([indico](#))
 - 05/2025 : XV ET Symposium @ Bologne ([indico](#))
- Des documents (avec une participation d'IJCLab)
 - 01/2025 : Functionalities required from the tools in support of the project management ([ET-PP D5.2](#))
 - 02/2025 : Refined Science Case ([ET-PP D6.1](#), aka Blue Book)
 - 04/2025 : The operational Project Office as a functional unit ([ET-PP D5.5](#))
 - 05/2025 : Filter cavity flexibility analysis ([ET-0098A-25](#)) => Task force design ([gitlab](#))

From the PBS to the Detector TDR




Detector TDR is an ET-PP deliverable.

Due date for draft was Sept. 2024

→ Postponed to end of 2025

Three inputs needed:

- Product Breakdown Structure (PBS);
with parameter tables
- Optical layout
- Detector layout

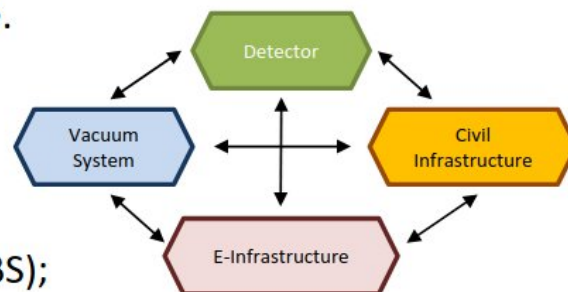

PBS (Product Breakdown Structure)

- ISB together with PO/Technical Coordinator
- PBS final structure is completed
- Parameter table submission
incl. description field (23786 parameters)
- Transfer to ET PBS Database & Json File
- Convert database content → latex files
- Pre-TDR: Check availability of descriptive reports
- Compose writing team
(asap; discussing logic of TDR structure)

Preliminary Detector TDR ET-PP milestone Feb. 2026



	Nomenclature	9
1	Introduction	19
2	Science Case Overview	21
3	Detector CDR Executive Summary	23
3.1	Main PBS upper systems design criteria summary	23
3.2	Overview of the main PBS systems, subsystems and their functional layouts and characteristics	23
3.3	Integration and installation requirements	23
3.4	Main elements (cost driver or technology challenges) functional and interfaces requirements, definitions	23
3.5	Results of R&D activities	23
3.5.1	Expected Results	23
3.5.2	Characterisation Methodology	23
3.5.3	Experimental Results obtained and TRL Evolution	23
3.5.4	Expected Impact (R&D by RSSd activity)	23
4	PBS element specifications and applied standards	25
4.1	Introduction	25
4.2	PBS elements specifications	25
4.3	PBS elements services and maintenance	25
4.4	PBS elements safety needs	25
4.5	Technical risk analysis of the PBS element	25
5	Detector Risk Analysis	27
6	Sustainability and Environment	29
7	costs	31
	Image credits	32



À venir

- Dates butoir

- Fin des mandats de SP et DPS : 22/03/2026
- Fin du mandat de CB chair : 15/11/2025
- Fin d'ET-PP : 08/2026

- Prochains meetings

- 30/06-01/07/2025 : ET-PP WP8 workshop : On site infrastructure, computing and data model @ Lyon ([indico](#))
- 22-24/07/2025 : ET-PP INFRA-DEV annual meeting @ Barcelone ([indico](#))
- 06-08/10/2025 : ET/Virgo France @ Lyon (à confirmer)
- 25-28/11/2025 : IV ET annual meeting @ Rijeka (Croatie) => dates à confirmer
